

Sandy Springs Veterans Park

March 2023 Project Update

Project Update

60% Design Documents 12/2022 TSPLOST Project Coordination 1/2023 95% Construction Documents 1/2023












Schedule Development 12/2022 Conceptual Pricing Review 1/2023



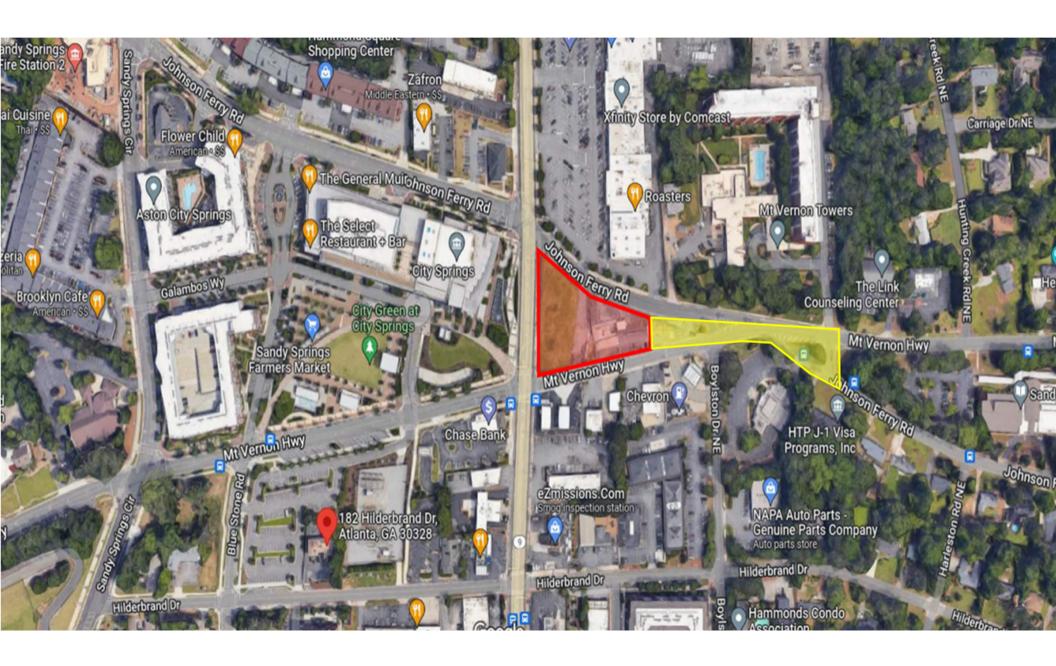

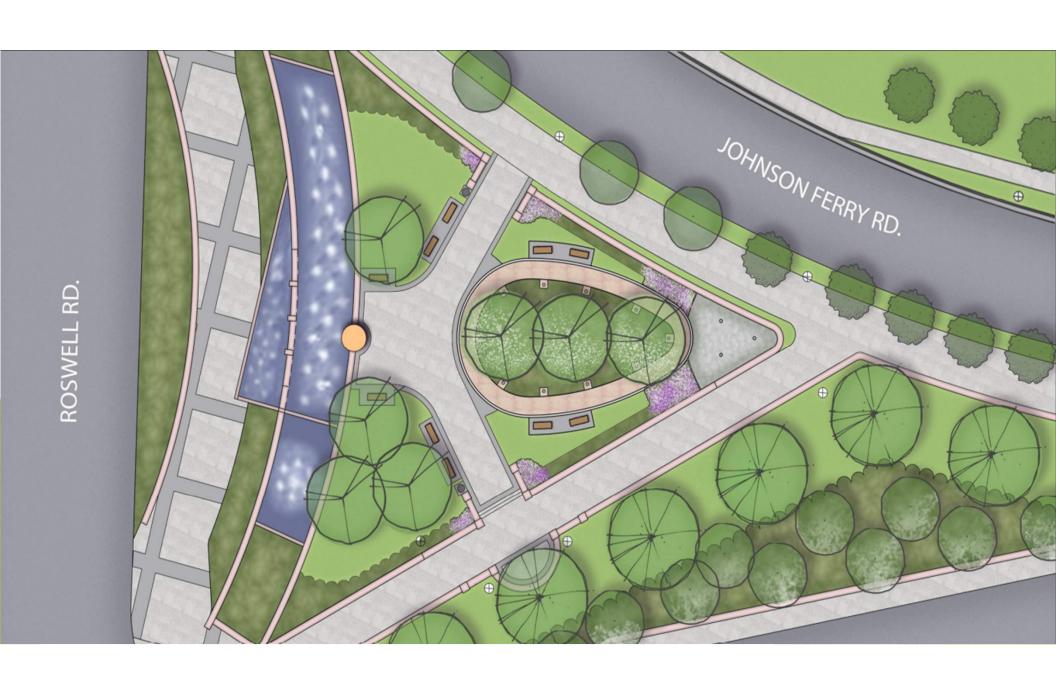

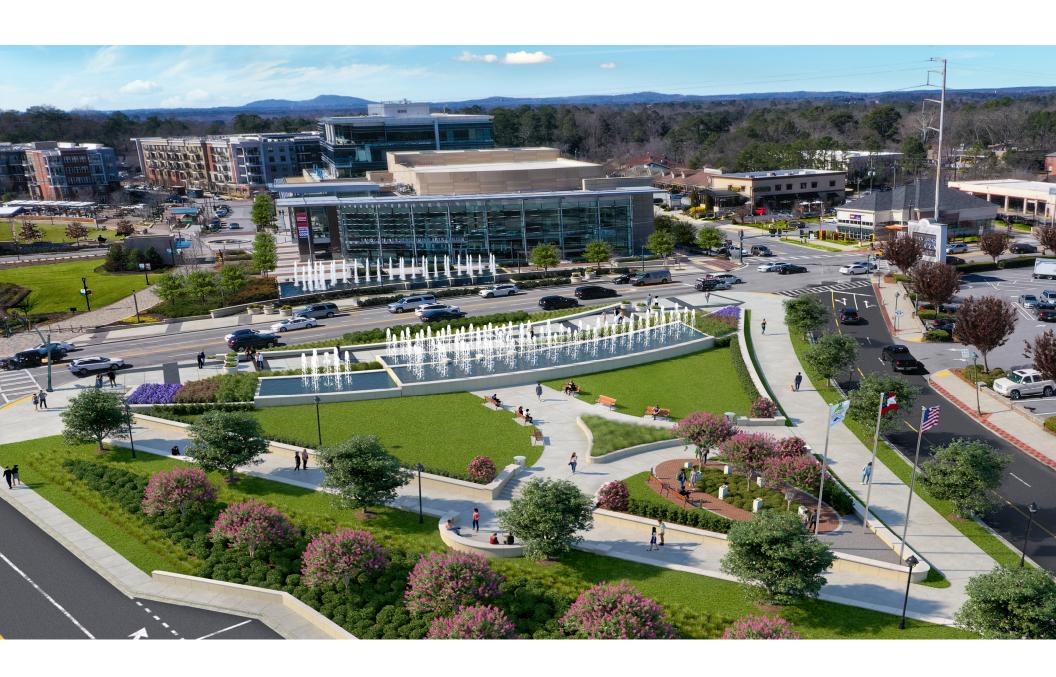





Project Schedule

TASK COMPLETION	TENTATIVE COMPLETION DATE
Groundbreaking	Week of March 20th
Grading	April 25 th
Fountain Structure	July 5 th
Fountain Finishes	August 8 th
Site Walls	August 29 th
Sidewalks	September 12 th
Site Lighting	September 26 th
Landscaping	September 28 th
Substantial Completion	October 1st
Final Completion	November 1st

Long Lead Items

DESCRIPTION	LEAD TIME
Fountain Mechanical Equipment	6 months
Electrical Gear & Components	4-6 months
Light Fixtures	3 months
Granite Stone Material	4 months
Hardscape Materials	3-6 months
Site Furnishings	3-4 months



Anticipated Total Construction Budget

Site Logistics	\$357,000
Erosion Control & Grading	\$384,912
Utilities	\$582,269
Hardscapes	\$508,391
Site Furnishings	\$164,624
Veterans Memorial Plaza	\$628,574
Landscaping & Irrigation	\$329,528
Fountain	\$1,484,285
Electrical	\$318,441
Construction Manager Contingency	\$140,352
Construction Manager Overheads	\$636,754
Value Management	(\$79,618)
TS-191 Credits	(\$183,589)
Owner Contingency	\$467,841
TOTAL DIRECT CONSTRUCTION COST	\$5,739,764

Anticipated Total Construction Budget

TOTAL DIRECT CONSTRUCTION COSTS	\$5,739,764
---------------------------------	-------------

AVAILABLE PROJECT FUNDING \$3,130,551


TOTAL ADDITIONAL FUNDS REQUESTED \$2,609,213


FIVE YEAR CIP FY2024 ASSUMPTION \$2,000,000

**Architect's Initial Estimated Budget \$4,747,802

No Fountain Option



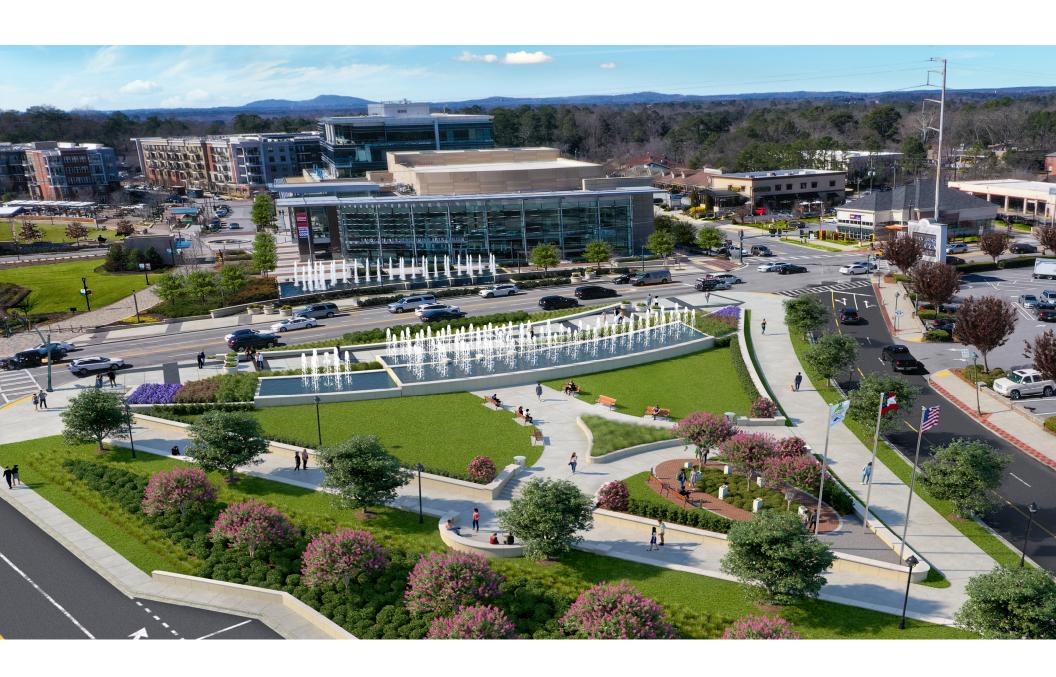

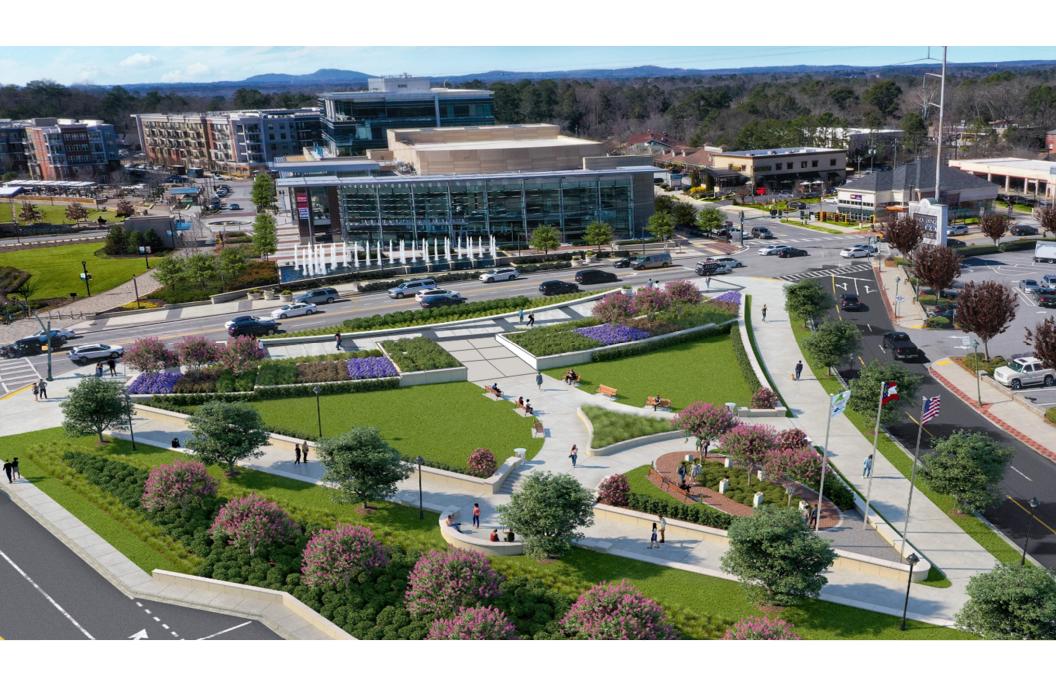

Anticipated Total Project Budget without the Fountain

Direct Construction Costs w/ Fountain	\$5,739,764.00
Remove Fountain	(\$1,484,285.00)
Add Planters/Irrigation/Sidewalks	\$794,945.00
TOTAL DIRECT COSTS OF CONSTRUCTION	\$5,050,424.00
AVAILABLE PROJECT FUNDING	\$3,130,551.00
TOTAL ADDITIONAL FUNDS REQUESTED	\$1,919,873.00

NEXT STEPS

Council Approval of GMP

Construction

03/2023 - RY Mobilization 10/2023 - Substantial Completion



Week of 03/20/2023
